

# 2006 SPLOST Project Profile Sheet

Updated 11-20-2007

**Project Entity:** Floyd County

**Project Name:** Huffaker Road Engineering and Right of Way

**Engineer:** Williams, Sweitzer & Barnum (Rome, GA)

**Contractor:**


**Status of Project:** Field Survey completed. Design phase 30% complete. Plan is to begin ROW acquisition for section of road from Fouche Gap Road to Big Texas Valley in first quarter of 2008.

**2006 SPLOST fund budget:** \$1,250,000 (\$94,440 spent to date).


**Other funding sources:**

**Total budget for project:** \$1,250,000

**Additional Information:**

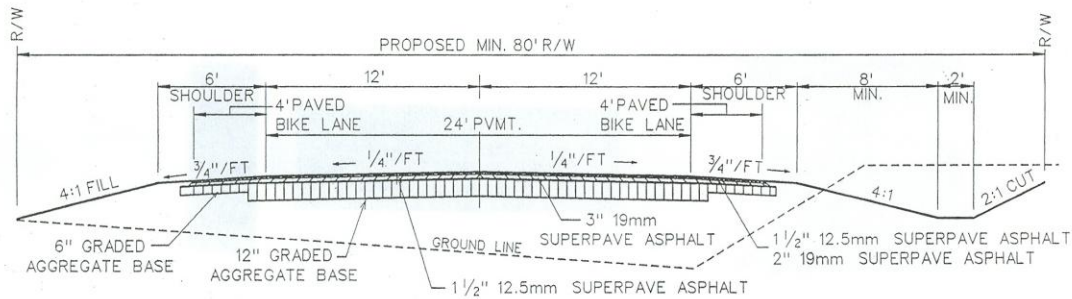

HUFFAKER ROAD  
TYPICAL ROAD SECTION  
NOT TO SCALE

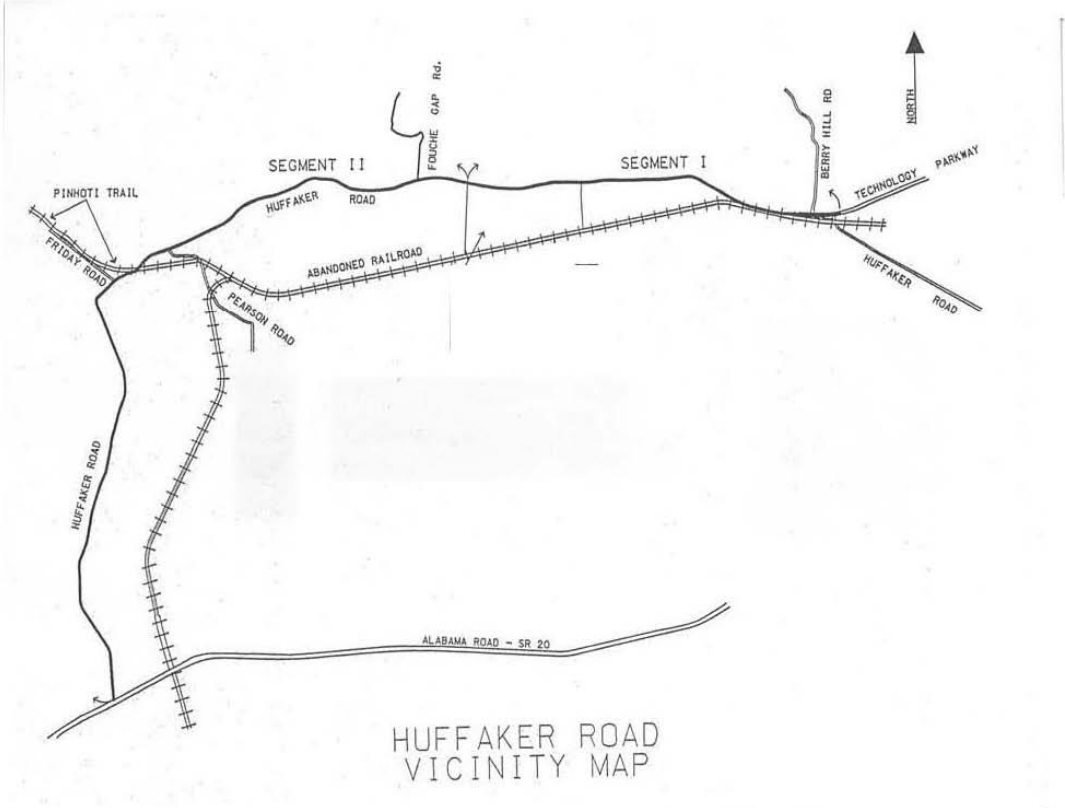

HUFFAKER ROAD  
VICINITY MAP
